

Halal Development Corporation

HALAL INTEGRATED PLATFORM (HIP) COMPLETION REPORT

HALAL DEVELOPMENT CORPORATION (HDC) BERHAD

HYPER ANALYTICS SDN. BHD.

Project

HALAL INTEGRATED PLATFORM 2.0

Customer

Halal Development Corporation Berhad

KPMG Tower, 5.02 Level 5,
47800 Petaling Jaya,
Selangor.

Document

Halal Integrated Platform Project Completion Report

Document Control

This document is under document control. All members of the distribution list will receive updated copies whenever alterations are made.

Contributors

Name	Role	Company	Contribution
Cik Aziela Shafarrah bt Zainal	Business Analyst	Hyper Analytics Sdn. Bhd.	Author
En. Fadzuan Bin Arbain	Project Manager	Hyper Analytics Sdn. Bhd.	Editor

Document Approval/Acceptance

Name	Role	Company
Tn Hj. Adly Mohamed	HIP Project Director	HDC HIP
En. Mohammad Hafiz B. Jamaluddin	HIP Project Manager	HDC HIP
Pn. Ema Juliany Bt. Jamaluddin	HIP Project Team Leader	HDC HIP
En. Ahmad Adli Hamizi Fairus	HIP Project Team Member	HDC HIP

Distribution List via Email

Name	Role	Company
Tn Hj. Adly Mohamed	Project Director	Halal Development Corporation
En. Mohammad Hafiz B. Jamaluddin	Project Manager	Halal Development Corporation
Pn. Ema Juliany Bt. Jamaluddin	Project Team Leader	Halal Development Corporation
Pn. Sakinah Ma'amor	Project Team Member	Halal Development Corporation
En. Ahmad Adli Hamizi Fairus	Project Team Member	Halal Development Corporation
En. Omar Shariff Abd Aziz	Project IT Team Member	Halal Development Corporation
En. Fadzuan bin Arbain	Project Manager	Hyper Analytics Sdn. Bhd.
Cik Aziela Shafarrah bt Zainal	Business Analyst	Hyper Analytics Sdn. Bhd.
Pn. Siti Norhidayah bt. Mohd Yusof	Application Manager	Hyper Analytics Sdn. Bhd.
En. Mohd Afiq Zulhafiz	Application Developer	Hyper Analytics Sdn. Bhd.
Cik Nadiah bt Mohd Nazri	Application Developer	Hyper Analytics Sdn. Bhd.

Document Acceptance

This document and its contents have been accepted by:



Prepared by:	Reviewed by:
Signature: 	**Signature:** 
Name: En. Fadzuan Bin Arbain	**Name:** Pn. Ema Juliany Bt. Jamaluddin
Role: Project Manager	**Role:** Project Team Leader
Organization: Hyper Analytics Sdn. Bhd.	**Organization:** Halal Development Corporation
Date: 11/10/2022	**Date:** 12/10/2022
Verified by:	**Approved by:**
Signature: 	**Signature:** 
Name: En. Mohammad Hafiz B. Jamaluddin	**Name:** Tn. Hj. Adly Mohamed
Role: Project Manager	**Role:** Project Director
Organization: Halal Development Corporation	**Organization:** Halal Development Corporation
Date: 12/10/2022	**Date:** 14/10/2022

Table of Contents

1 Introduction 6
1.1 Abbreviation 7
2 Project Background 8
2.1 Project Scope 9
2.2 Project Objectives 10
3 Implementation Schedule 11
4 Project Milestones 19
5 Summary 22
6 Appendix 23
Introduction 24
Objective 24
Document Structure 24
Abbreviation 25
Scope of Works 26
Release 1 30
Release 2 33
Release 3 36
Release 4 37
Release 5 40
Deliverables 43
Certificates 45

1 Introduction

This document is intended to describe the Halal Integrated Platform (HIP) Project Completion Report for the Halal Integrated Platform (HIP) project. This document is the final deliverable of the project that indicates the project has successfully delivered to Halal Development Corporation (HDC).

It is the final milestone of the HIP project and indicates that all the phases in the system implementation lifecycle have been completed successfully.

The HIP Project Completion Report is the product of the various test and discussions that was held between the Vendor and a specified HDC department which is HIP which will be the owner of this entire solution and will be responsible for the technical support for the solution.

There were 3 main phases in the entire project implementation lifecycle which are:

1. Configuration Assessment and Customization;
2. HIP Deployment; and
3. HIP Release.

The purpose for the first phase which is the Configuration Assessment and Customization was the Customized the integration between third party with HIP.

The purpose for the second phase which is the HIP Deployment is to ensure the HIP project had been deployed and deliver as per schedule.

The purpose for the final phase which is the HIP release are to conduct user acceptance test and training on how to use the application and the deliverables for each release was the UAT, user manual, ToT reports and this completion report.

As the outcome of all the phases mentioned above the final details of the project was compiled in this Report document as follows:

Chapter 1: Introduction of this Project Completion Report is an Introduction to the document.

Chapter 2: Project Background of this Project Completion Report will be the write-up on the details of scope and objectives of this project.

Chapter 3: Project Milestones of this Project Completion Report will be the write-up on the important project milestones and completion dates of the milestones of the project.

Chapter 4: Summary of this Report will be the summary of the entire project.

1.1 Abbreviation

All the abbreviation in this document is as listed in the table below.

Term	Definition
HIP	Halal Integrated Platform
HDC	Halal Development Corporation
ToT	Transfer of Technology
UAT	User Acceptance Test
MSMEs	Micro, Small Medium Enterprises
CRM	Customer Relationship Management
DASH	Digital Augmented Reality Showcase of Halal Malaysia
HART	Halal Accelerator Tools
HTI	Halal Training Institute
NFC	Near Field Communication

2 Project Background

HDC aims to create a new and bigger marketspace for Malaysia's Halal products and services by developing effective market access strategies for Malaysian companies to have a greater local and international presence. The Halal industry has grown quite rapidly due to the increased Halal awareness and the surge in consumer demands for halal products and services in Muslim and non-Muslim countries throughout the world.

As the custodian of Malaysia's Halal Economy, Halal Development Corporation (HDC) is entrusted by Malaysian Government to spearhead the development of Malaysia's Halal ecosystem and infrastructure in positioning Malaysia as the most competitive country leading the global Halal Industry. HDC is taking measures to strengthen their position as a driver for industry growth by targeting Micro, Small and Medium Enterprises (MSMEs) involved in Halal related sectors and services in order to potentially grow Malaysia Halal export value.

Halal Integrated Platform (HIP) is anticipated to become the one stop center for Halal Industry players particularly the Micro, Small, and Medium Enterprise (MSME) operator to grow their business through the Halal Ecosystem. Via the new HIP platform, HDC envisions a more centralized monitoring and management of Halal Industry growth. Provisioning of its services can channel in a one-stop center and its value notable globally.

2.1 Project Scope

The scope of this project is to deliver the modules essential for each release as a core functional in HIP project. Each release and its modules are described in table below:

Release	Modules
Release 1	• Portal • Internal Portal • Business Profile • Social Media • CRM
Release 2	• SMEXpert • Integration eMarket Place • HIPER • Halal Knowledge Centre • DASH • Halal Ingredient Database • HIP Percipio • PayHalal • Business Intelligence
Release 3	• Mobile Apps • eProcurement • HIP Rating
Release 4	• HANA Chatbot • Integration SME Assist • Integration Micro Leap • Integration Easy Store • Integration TFX Islamic • Purchase Request/Product Request/Ingredient • Halal Professional Feature
Release 5	• eMarketPlace • Customer Knowledge Help Centre • Business Matching • Feature to transfer company details to another individual • 2 Star Rating to get halal Verified by Global Haltech • HIP Credit for advertisement / referral program/feature or sponsorship • Bulk Registration Module • Mailing List

2.2 Project Objectives

The main objective of the project is to deliver an effective and efficient business platform as one stop center and capable enough to handle many businesses user to suite their business needs. The other objectives of HIP as listed below:

1. Catalysing globalisation opportunities through the market acceleration and access;
2. Nurturing and facilitation local Halal SME's to be an established Halal supplier for local and international market;
3. To be the One Stop Centre that connects and enable Halal industry players to take part in the Halal ecosystem;
4. Provide industrial insight through collective knowledge, expertise, data and tool that empower the industry;
5. Enabling Halal business to leverage on digital space in expanding their market outreach; and
6. Connecting business with the Halal business experts through the halal network and ecosystem.

3 Implementation Schedule

Task Name	Duration	Start	Finish
Start	320.5 days	Mon 6/21/21	Fri 10/14/22
Release 1	143.8 days	Mon 6/21/21	Mon 1/17/22
Requirement Study & Design	**140 days**	**Mon 6/21/21**	**Tue 1/11/22**
Portal	5 days	Mon 6/21/21	Fri 6/25/21
Internal Portal	5 days	Mon 6/28/21	Fri 7/2/21
Business profile	5 days	Mon 7/5/21	Fri 7/9/21
Social Media	10 days	Mon 6/21/21	Fri 7/2/21
CRM	5 days	Mon 7/5/21	Fri 7/9/21
Release 1 SRDS Draft Review	5 days	Mon 7/12/21	Mon 1/10/22
Release 1 SRDS Approval	1 day	Tue 1/11/22	Tue 1/11/22
Release 1 SRDS	0 days	Tue 1/11/22	Tue 1/11/22
Development / Configuration	**28 days**	**Wed 7/21/21**	**Wed 9/1/21**
Portal	20 days	Wed 7/21/21	Thu 8/19/21
Internal Portal	8 days	Fri 8/20/21	Wed 9/1/21
Business profile	18 days	Wed 7/21/21	Tue 8/17/21
Social Media	28 days	Wed 7/21/21	Wed 9/1/21
CRM	10 days	Wed 8/18/21	Wed 9/1/21
Testing	**121.8 days**	**Wed 7/21/21**	**Fri 1/14/22**
Develop Phase 1 Test Scenario	5 days	Wed 7/21/21	Tue 7/27/21
Develop Phase 1 UAT Testscript	**113.4 days**	**Wed 7/28/21**	**Tue 1/11/22**
Portal	2 days	Wed 7/28/21	Mon 1/10/22
Internal Portal	2 days	Fri 7/30/21	Mon 1/10/22
Business profile	2 days	Tue 8/3/21	Mon 1/10/22
Social Media	2 days	Thu 8/5/21	Mon 1/10/22
CRM	2 days	Wed 8/11/21	Tue 1/11/22
Conduct UAT Session	**100.8 days**	**Wed 8/18/21**	**Tue 1/11/22**
Portal	0.5 days	Fri 8/20/21	Mon 1/10/22
Internal Portal	0.5 days	Thu 9/2/21	Mon 1/10/22

Task Name	Duration	Start	Finish
Business profile	0.5 days	Wed 8/18/21	Mon 1/10/22
Social Media	0.5 days	Thu 9/2/21	Mon 1/10/22
CRM	0.5 days	Thu 9/2/21	Tue 1/11/22
Release 1 UAT Acceptance	3 days	Tue 1/11/22	Fri 1/14/22
Release 1 Deployment	1 day	Fri 1/14/22	Mon 1/17/22
Release 2	133.6 days	Wed 7/21/21	Fri 2/4/22
Requirement Study & Design	122.5 days	Wed 7/21/21	Mon 1/17/22
Integration	**10 days**	**Wed 7/21/21**	**Tue 8/3/21**
SMEXpert App	5 days	Wed 7/21/21	Tue 7/27/21
E-Marketplace (talentexchange)	5 days	Wed 7/21/21	Tue 7/27/21
HIPER	5 days	Wed 7/21/21	Tue 7/27/21
Halal Knowledge Centre (jomSettle)	5 days	Wed 7/21/21	Tue 7/27/21
Digital Augmented Reality Showcase of Halal Malaysia (DASH)	5 days	Wed 7/28/21	Tue 8/3/21
Halal Ingredient Database	5 days	Wed 7/28/21	Tue 8/3/21
HTI Percipio	5 days	Wed 7/28/21	Tue 8/3/21
PayHalal	5 days	Wed 7/28/21	Tue 8/3/21
Business Intelligence	10 days	Wed 7/21/21	Tue 8/3/21
Release 2 SRDS Draft Review	5 days	Wed 8/4/21	Fri 1/14/22
Release 2 SRDS Approval	1 day	Fri 1/14/22	Mon 1/17/22
Release 2 SRDS	0 days	Mon 1/17/22	Mon 1/17/22
Development / Configuration	111.5 days	Mon 8/16/21	Tue 1/25/22
Integration	111.5 days	Mon 8/16/21	Tue 1/25/22
SMEXpert App	5 days	Mon 8/16/21	Fri 8/20/21
Digital Augmented Reality Showcase of Halal Malaysia (DASH)	5 days	Mon 8/16/21	Fri 8/20/21
Halal Ingredient Database	10 days	Mon 8/23/21	Mon 9/6/21
PayHalal	5 days	Mon 8/23/21	Thu 1/20/22
HIPER	10 days	Mon 8/23/21	Tue 1/25/22
Halal Knowledge Centre (Jomsettle)	10 days	Mon 8/16/21	Fri 8/27/21
Percipio	5 days	Mon 8/30/21	Thu 1/20/22

Task Name	Duration	Start	Finish
E-Marketplace (talentexchange)	10 days	Mon 8/23/21	Mon 9/6/21
Business Intelligence	15 days	Mon 8/16/21	Fri 1/21/22
Testing	101.6 days	Tue 9/7/21	Thu 2/3/22
Develop Test Scenario	3 days	Tue 9/7/21	Thu 9/9/21
Develop TestScript UAT	2 days	Fri 9/10/21	Wed 1/26/22
Conduct UAT Session	**94.1 days**	**Tue 9/14/21**	**Fri 1/28/22**
Integration	**93.7 days**	**Tue 9/14/21**	**Fri 1/28/22**
HIPER	0.5 days	Wed 1/26/22	Wed 1/26/22
Halal Knowledge Centre	0.5 days	Tue 9/14/21	Thu 1/27/22
Digital Augmented Reality Showcase of Halal Malaysia (DASH)	0.5 days	Wed 9/15/21	Thu 1/27/22
Halal Ingredient Database	0.5 days	Wed 9/15/21	Thu 1/27/22
Percipio	0.5 days	Fri 9/17/21	Thu 1/27/22
PayHalal	0.5 days	Thu 1/27/22	Fri 1/28/22
E-Marketplace	0.5 days	Mon 9/20/21	Fri 1/28/22
SMEXpert App	0.5 days	Mon 9/20/21	Fri 1/28/22
Business Intelligence	0.5 days	Tue 9/21/21	Fri 1/28/22
Release 2 UAT Acceptance	2 days	Fri 1/28/22	Thu 2/3/22
Release 2 Deployment	1 day	Thu 2/3/22	Fri 2/4/22
Release 3	138.5 days	Mon 8/16/21	Wed 3/9/22
Requirement Study & Design	114.5 days	Mon 8/16/21	Fri 1/28/22
eProcurement	10 days	Mon 8/16/21	Fri 8/27/21
Mobile Apps	10 days	Mon 8/16/21	Fri 8/27/21
HIP Rating	10 days	Mon 8/16/21	Fri 8/27/21
Release 3 SRDS Draft Review	10 days	Mon 8/30/21	Thu 1/27/22
Release 3 SRDS Approval	1 day	Thu 1/27/22	Fri 1/28/22
Release 3 SRDS	0 days	Fri 1/28/22	Fri 1/28/22
Development / Configuration	**105.5 days**	**Wed 9/15/21**	**Thu 2/17/22**
eProcurement	20 days	Wed 9/15/21	Thu 2/17/22
Mobile Apps	20 days	Wed 9/15/21	Thu 2/3/22

Task Name	Duration	Start	Finish
HIP Rating	20 days	Wed 9/15/21	Wed 10/13/21
Testing	96.5 days	Thu 10/14/21	Tue 3/8/22
Develop Test Scenario	5 days	Thu 10/14/21	Mon 2/21/22
Develop TestScript UAT	5 days	Mon 2/21/22	Wed 3/2/22
Conduct UAT Session	**1 day**	**Wed 3/2/22**	**Thu 3/3/22**
eProcurement	0.5 days	Wed 3/2/22	Wed 3/2/22
Mobile Apps	0.5 days	Thu 3/3/22	Thu 3/3/22
Release 3 UAT Acceptance	3 days	Thu 3/3/22	Tue 3/8/22
Release 3 Deployment	1 day	Tue 3/8/22	Wed 3/9/22
Infrastructure and Configuration	**40 days**	**Sat 7/31/21**	**Thu 9/30/21**
Install Production HIP 2.0	15 days	Sat 7/31/21	Tue 8/24/21
Data Migration of pre-registered	15 days	Wed 8/25/21	Wed 9/15/21
Data Migration Test / Validation	5 days	Fri 9/17/21	Thu 9/23/21
Data Migration Report	5 days	Fri 9/24/21	Thu 9/30/21
Version 1 Documentation	142.4 days	Wed 9/8/21	Wed 4/6/22
Documentation	90.4 days	Fri 10/1/21	Fri 2/11/22
User Manual Write-up	10 days	Fri 10/1/21	Thu 1/13/22
Admin Manual Write-up	10 days	Fri 10/15/21	Thu 1/27/22
Application Configuration Documentation Write-up	11 days	Mon 11/1/21	Mon 2/7/22
System Documentation Write-up	10 days	Wed 11/17/21	Fri 2/11/22
Training & Technology Transfer (TOT)	142.4 days	Wed 9/8/21	Wed 4/6/22
Develop Training Materials	**127 days**	**Wed 9/8/21**	**Wed 3/16/22**
Release 1 Training	5 days	Wed 9/8/21	Thu 1/20/22
Release 2 Training	5 days	Fri 2/4/22	Fri 2/11/22
Release 3 Training	5 days	Wed 3/9/22	Wed 3/16/22
Internal User Training	**127 days**	**Wed 9/15/21**	**Wed 3/23/22**
Release 1 Training	5 days	Wed 9/15/21	Mon 1/24/22
Release 2 Training	5 days	Fri 2/11/22	Fri 2/18/22
Release 3 Training	5 days	Wed 3/16/22	Wed 3/23/22

Task Name	Duration	Start	Finish
Internal Admin Training	5 days	Mon 11/22/21	Fri 3/25/22
Internal Technical Training	5 days	Fri 3/25/22	Fri 4/1/22
External User Training	2 days	Mon 12/6/21	Fri 4/1/22
Training Completion Report	3 days	Fri 4/1/22	Wed 4/6/22
Release 4	59.5 days	Mon 1/10/22	Fri 4/8/22
Requirement Study & Design	22 days	Mon 1/10/22	Fri 2/11/22
HANA Chatbot	5 days	Mon 1/10/22	Fri 1/14/22
Integration - HTI Training Registration	5 days	Mon 1/17/22	Mon 1/24/22
Integration - MicroLeap/Online Business Card (Integration CTOS)	5 days	Tue 1/25/22	Mon 1/31/22
Integration - EasyStore	5 days	Tue 1/25/22	Mon 1/31/22
Integration - TFX Islamic	5 days	Tue 1/25/22	Mon 1/31/22
Purchase Request/Product Request/Ingredient	10 days	Mon 1/17/22	Mon 1/31/22
Halal Professional Feature	5 days	Tue 1/25/22	Mon 1/31/22
Release 4 SRDS Draft Review	5 days	Thu 2/3/22	Wed 2/9/22
Release 4 SRDS Approval	1 day	Thu 2/10/22	Thu 2/10/22
Release 4 SRDS	1 day	Fri 2/11/22	Fri 2/11/22
Development / Configuration	28 days	Mon 2/14/22	Fri 3/25/22
HANA Chatbot	20 days	Mon 2/14/22	Tue 3/15/22
Integration - HTI Training Registration	8 days	Wed 3/16/22	Fri 3/25/22
Integration - MicroLeap/Online Business Card/CTOS	8 days	Wed 3/16/22	Fri 3/25/22
Integration - EasyStore	8 days	Wed 3/16/22	Fri 3/25/22
Integration - TFX Islamic	18 days	Mon 2/14/22	Fri 3/11/22
Purchase Request/Product Request/Ingredient	20 days	Mon 2/14/22	Tue 3/15/22
Halal Professional Feature	10 days	Mon 3/14/22	Fri 3/25/22
Testing	36.5 days	Mon 2/14/22	Thu 4/7/22
Develop Phase 4 Test Scenario	14 days	Mon 2/14/22	Mon 3/7/22
Develop Phase 4 UAT Testscript	**12 days**	**Mon 3/14/22**	**Tue 3/29/22**
HANA Chatbot	2 days	Wed 3/16/22	Thu 3/17/22
Integration - HTI Training Registration	2 days	Mon 3/28/22	Tue 3/29/22

Task Name	Duration	Start	Finish
Integration - MicroLeap	2 days	Mon 3/28/22	Tue 3/29/22
Integration - EasyStore	2 days	Mon 3/28/22	Tue 3/29/22
Integration - TFX Islamic	2 days	Mon 3/14/22	Tue 3/15/22
Purchase Request/Product Request/Ingredient	2 days	Wed 3/16/22	Thu 3/17/22
Halal Professional Feature	2 days	Mon 3/28/22	Tue 3/29/22
Conduct UAT Session	**3.5 days**	**Wed 3/30/22**	**Mon 4/4/22**
HANA Chatbot	0.5 days	Wed 3/30/22	Wed 3/30/22
Integration - HTI Training Registration	0.5 days	Wed 3/30/22	Wed 3/30/22
Integration - MicroLeap	0.5 days	Thu 3/31/22	Thu 3/31/22
Integration - EasyStore	0.5 days	Thu 3/31/22	Thu 3/31/22
Integration - TFX Islamic	0.5 days	Fri 4/1/22	Fri 4/1/22
Purchase Request/Product Request/Ingredient	0.5 days	Fri 4/1/22	Fri 4/1/22
Halal Professional Feature	0.5 days	Mon 4/4/22	Mon 4/4/22
Release 4 UAT Acceptance	3 days	Mon 4/4/22	Thu 4/7/22
Release 4 Deployment	1 day	Thu 4/7/22	Fri 4/8/22
Release 5	101.5 days	Mon 3/28/22	Thu 9/1/22
Requirement Study & Design	40.5 days	Mon 3/28/22	Thu 6/2/22
E-Marketplace Integration/Integration (Pukalshop)	5 days	Mon 3/28/22	Fri 4/1/22
Customer Ctr Knowledge Base (FAQ) + Live Chat	5 days	Mon 4/4/22	Fri 4/8/22
Business matching feature for mobile apps	5 days	Mon 4/11/22	Fri 4/15/22
Feature to transfer company details to other individual	5 days	Fri 4/8/22	Fri 4/15/22
2 Star Rating to get Halal Verified by Global Haltech	5 days	Fri 4/15/22	Tue 4/26/22
HIP Credit for advertisement/ referal program/feature or sponsorship (API for Public View - NFC card integration) + HIP Marketing	5 days	Tue 4/26/22	Tue 5/10/22
Bulk Registration Module	5 days	Tue 5/10/22	Wed 5/18/22
Mailing List	5 days	Wed 5/18/22	Wed 5/25/22
Release 5 SRDS Draft Review	5 days	Wed 5/25/22	Wed 6/1/22
Release 5 SRDS Approval	1 day	Wed 6/1/22	Thu 6/2/22
Release 5 SRDS	0 days	Thu 6/2/22	Thu 6/2/22
Development / Configuration	**48 days**	**Thu 5/26/22**	**Fri 8/5/22**

Task Name	Duration	Start	Finish
E-Marketplace	5 days	Thu 6/2/22	Fri 6/10/22
Customer Ctr Knowledge Base (FAQ) + Live Chat	5 days	Thu 5/26/22	Tue 6/14/22
Business matching feature for mobile apps	10 days	Thu 6/2/22	Fri 6/17/22
Feature to transfer company details to other individual	5 days	Fri 6/17/22	Fri 6/24/22
2 Star Rating to get Halal Verified by Global Haltech	10 days	Thu 6/2/22	Fri 6/17/22
HIP Credit for advertisement/ referal program/feature or sponsorship (API for Public View - NFC card integration)	11 days	Fri 6/17/22	Mon 7/4/22
Bulk Registration Module	11 days	Mon 7/4/22	Thu 7/21/22
Mailing List	11 days	Thu 7/21/22	Fri 8/5/22
Testing	**60 days**	**Thu 6/2/22**	**Tue 8/30/22**
Develop Test Scenario	10 days	Thu 6/2/22	Fri 6/17/22
Develop TestScript UAT	**38 days**	**Fri 6/17/22**	**Fri 8/12/22**
E-Marketplace	5 days	Fri 6/17/22	Fri 6/24/22
Customer Ctr Knowledge Base (FAQ) + Live Chat	5 days	Fri 6/17/22	Fri 6/24/22
Business matching feature for mobile apps	5 days	Fri 6/17/22	Fri 6/24/22
Feature to transfer company details to other individual	5 days	Fri 6/24/22	Fri 7/1/22
2 Star Rating to get Halal Verified by Global Haltech	5 days	Fri 6/17/22	Fri 6/24/22
HIP Credit for advertisement/ referal program/feature or sponsorship (API for Public View - NFC card integration)	5 days	Mon 7/4/22	Wed 7/13/22
Bulk Registration Module	5 days	Thu 7/21/22	Thu 7/28/22
Mailing List	5 days	Fri 8/5/22	Fri 8/12/22
Conduct UAT Session	**8 days**	**Fri 8/12/22**	**Wed 8/24/22**
E-Marketplace	1 day	Fri 8/12/22	Mon 8/15/22
Customer Ctr Knowledge Base (FAQ) + Live Chat	1 day	Mon 8/15/22	Tue 8/16/22
Business matching feature for mobile apps	1 day	Tue 8/16/22	Wed 8/17/22
Feature to transfer company details to other individual	1 day	Wed 8/17/22	Thu 8/18/22
2 Star Rating to get Halal Verified by Global Haltech	1 day	Thu 8/18/22	Fri 8/19/22
HIP Credit for advertisement/ referal program/feature or sponsorship (API for Public View - NFC card integration)	1 day	Fri 8/19/22	Mon 8/22/22
Bulk Registration Module	1 day	Mon 8/22/22	Tue 8/23/22
Mailing List	1 day	Tue 8/23/22	Wed 8/24/22
Release 5 UAT Acceptance	4 days	Wed 8/24/22	Tue 8/30/22

Task Name	Duration	Start	Finish
Release 5 Deployment	1 day	Tue 8/30/22	Thu 9/1/22
Version 2 Documentation	**71 days**	**Thu 5/19/22**	**Thu 9/1/22**
Documentation	**41 days**	**Thu 5/19/22**	**Wed 7/20/22**
User Manual Write-up	10 days	Thu 5/19/22	Thu 6/2/22
Admin Manual Write-up	10 days	Thu 6/2/22	Fri 6/17/22
Application Configuration Documentation Write-up	11 days	Fri 6/17/22	Mon 7/4/22
System Documentation Write-up	10 days	Mon 7/4/22	Wed 7/20/22
Training & Technology Transfer (TOT)	**30 days**	**Wed 7/20/22**	**Thu 9/1/22**
Develop Training Materials	**10 days**	**Wed 7/20/22**	**Wed 8/3/22**
Release 4 Training	5 days	Wed 7/20/22	Wed 7/27/22
Release 5 Training	5 days	Wed 7/27/22	Wed 8/3/22
Internal User Training	**10 days**	**Wed 8/3/22**	**Wed 8/17/22**
Release 4 Training	5 days	Wed 8/3/22	Wed 8/10/22
Release 5 Training	5 days	Wed 8/10/22	Wed 8/17/22
Internal Admin Training	5 days	Wed 8/17/22	Wed 8/24/22
Internal Technical Training	5 days	Wed 8/24/22	Thu 9/1/22
Security Posture Assessment (SPA) -Stress Test/ Security Testing	**30 days**	**Thu 9/1/22**	**Thu 10/13/22**
3rd Party Testers Performs Test / Penetration Test & Load Test	20 days	Thu 9/1/22	Thu 9/29/22
SPA Completion Report/ Test Report	10 days	Thu 9/29/22	Thu 10/13/22
System Full Go-Live	1 day	Thu 10/13/22	Fri 10/14/22
Project Closure	0 days	Fri 10/14/22	Fri 10/14/22

4 Project Milestones

In the table below described the main project milestones and the completion dates for each milestone. The details of the milestones will be described later on this section.

No.	Milestone	Completion Date
1.	HIP Project Kick-off	25th Jun 2021
2.	Requirements Study & Design Specification (Release 1)	7th Feb 2022
3.	UAT Release 1	26th May 2022
4.	Deployment (Release 1)	29th May 2022
5.	Requirements Study & Design Specification (Release 2)	27th May 2022
6.	UAT Release 2	7th June 2022
7.	Deployment (Release 2)	10th June 2022
8.	Requirements Study & Design Specification (Release 3)	26th June 2022
9.	UAT Release 3	28th July 2022
10.	Deployment (Release 3)	29th July 2022
11.	ToT Release 1,2 and 3 – Admin Training	29th Aug 2022
12.	ToT Release 1,2 and 3 – End User Training	14th Sep 2022
13.	Requirements Study & Design Specification (Release 4)	22nd Aug 2022
14.	UAT Release 4	5th Sep 2022
15.	Deployment (Release 4)	10th Sep 2022
16.	Requirements Study & Design Specification (Release 5)	16th Sep 2022
17.	UAT Release 5	20th Sep 2022
18.	Deployment (Release 5)	23rd Sep 2022
19.	ToT Release 4 and 5 – Admin Training	4th Oct 2022
20.	ToT Release 4 and 5 – End User Training	5th Oct 2022
21.	System Commissioning & Completion Report Submission	14th Oct 2022

Project Kick-off – This milestone indicates the project has been started officially. The activities involved in this milestone include:

- Identify the project organization chart and get to know with the project team;
- Set the expectation and the scope of the project;
- Share the project implementation schedule;
- Set meeting's date for Requirements Study & Design Specification;
- Identify the required items from HIP's project team for the project.

Requirements Study & Design Specification – This milestone indicates that all the requirements for the solution was gathered and compiled and assess as an input to develop the HIP module. The activities involved in this milestone includes:

- Gap Analysis session to identify the requirement's changes needed for the module covered on each release.
- User requirements gathering session to gather new requirements of the HIP project.
- Identify the detailed features and functions for HIP module.
- Discussion between Vendor, HDC and third party on integration modules.

HIP Deployment – This milestone indicates that all the required modules had been installed successfully on the production server. The activities involved in this milestone include:

- HIP's project team ensure all the core modules and all its pre-requisites had been successfully installed;
- Install HIP module based on release for production environment;
- Installation Test to indicate all the modules had been installed successfully.

User Acceptance Test (UAT) & User Training (ToT) – This milestone indicates that all the required modules and their features are according to the specification given. The activities involved in this milestone include:

- HIP's project team ensures all the core components and all the modules had been successfully deployed.
- UAT's Test script write-up for the UAT session.
- UAT session with HDC to test the features and functions of delivered modules based on release in HIP.
- User Manual write-up for the ToT session.
- Training session with HDC on the features and functions of delivered modules based on release.
- Compile and document all the activities done during UAT & ToT sessions and produce the UAT & ToT report.

System Commissioning – This milestone indicates that the new solution is ready for production. The activities involved in this milestone include:

- HIP's project team ensures all the core components and all the HIP modules had been successfully deployed.
- Produce Project Completion Report for signed-off.

5 Summary

By implementing this project, the objectives of this project are successfully accomplished and expectantly this platform will become the well-known one stop center for Halal Industry players within Malaysia and across the nationwide.

6 Appendix

Below is appendix as for reference.

Introduction

This document is the Final Acceptance Test (FAT) Report for Halal Integrated Platform (HIP) Release 1 to 5. This document is intended to describe the acceptance test for all features and functionality of HIP based on the System Requirement & Design Specification (SRDS).

Upon acceptance by Halal Development Corporation (HDC), the FAT Report will be the initiation of the next phase which is the Release Phase. In Release Phase, it will include training and production setup ready.

The Final Acceptance Testing Report is produced based on modules deployed into production environment by vendor and acceptance by HDC. The modules deployed will be discussed later on Chapter 3.

Objective

The objective of this report is to record the modules deliverable acceptance in production which were verified against the module's specification.

Document Structure

The document is structured as follows:

Chapter 1: Introduction.

Chapter 2: Scope of works.

Chapter 3: Deliverables of modules.

Chapter 4: FAT Certificate

Abbreviation

All the abbreviation in this document is as listed in the table below.

Table 1: Abbreviation

Term	Definition
HIP	Halal Integrated Platform
HDC	Halal Development Corporation
ToT	Transfer of Technology
FAT	Final Acceptance Test
MSMEs	Micro, Small Medium Enterprises
CRM	Customer Relationship Management
DASH	Digital Augmented Reality Showcase of Halal Malaysia
HART	Halal Accelerator Tools
HTI	Halal Training Institute
NFC	Near Field Communication

Scope of Works

In general HIP will have the functionalities as listed below:

1. To establish HIP as a One-Stop-Centre for service delivery and industry engagement;
2. To achieve a single point of data entry with the objective of having a single consolidated view of information;
3. To move towards a fully integrated system;
4. To improve timely flow of data between departments in HDC;
5. To be able to support and maintain mission-critical information;
6. To increase data integrity through minimising manual intervention in transaction processing;
7. To provide a single organisation-wide view of HDC's information databases and repositories to support the strategic planning and implementation effort;
8. To improve accessibility to systems and ICT tools for all HDC staff at all levels; and
9. To automate HIP with the objective of increasing efficiency and raising the level of effectiveness by ensuring key applications are available, relevant and adequate.

HIP Design and implementation

1. Vendor is to provide advice in designing HIP that focus on User Experience and System Usability;
2. Vendor is to provide advice in designing platform and the terms and conditions that conforms to related Acts such as *Personal Data Protection Act*, and other related legal compliance;
3. Develop, configure and customize the Halal Integrated Platform (HIP) according to HDC requirement and functionalities stated in the compliance table in Appendix 4 (HIP TOR Functional Requirement);
4. Develop and configure the portal capability to support Social Media, Business Profiling, Customer Relationship Management, Business Directory, eProcurement, and Business Intelligence;
5. Enterprise *Social Networking* platform functions to allow users to perform social networking features such as like/rate, follow, message and share formally and informally;
6. Design and configuration of *Workflow Management* with built-in workflow process with configuration capability;
7. Support for *Metrics Reporting* (e.g. generating search and usage analytics) to allow insights of activities and usage such as user activities on each module, lead conversion and others;
8. To integrate with HDC third party application such as Halal Knowledge Centre (HKC), Digital Augmented / Virtual Reality Showcase of Halal Malaysia (DASH), HIPER portal, Halal Ingredient Database and eMarketplace;

9. Design and develop HIP *API Library* for future external integration; and
10. Vendor is responsible for the creation of procedures and processes related to the solution implementation and data migration (if required).

Technical setup, installation, hardware and software recommendation

1. Vendor is required to propose the hardware, infrastructure, appliances, server, and software that are necessary for this successful implementation of the solution are to be proposed and catered for the period of 1 year;
2. Vendor will need to prepare their own development, testing and deployment infrastructure to be utilize for the implementation of the HIP;
3. Vendor should configure and setup the hardware and software accordingly at various tests, DR, staging and production environments for any setup specific to HIP;
4. The infrastructure should support High Availability (HA);
5. If required all cabling to be catered by vendor; and
6. Vendor to include projection cost of operation for the next 3 years of HIP after Go Live, with the assumption of 40% user growth yearly.

System Integration

1. Assist in the creation of procedures and processes related to the solution integration between systems;
2. Supply, deliver, configure, test and commission the integration between systems;
3. The HIP should have the capabilities to integrate with other systems. Some of the potential integration systems in HDC are Halal Knowledge Centre (HKC), Digital Augmented / Virtual Reality Showcase of Halal Malaysia (DASH), HIPER portal, Halal Ingredient Database and e-Marketplace. All integration should allow for future implementation; and
4. Vendor is required to support and work the applications' vendor and application team during the implementation of the integration with HIP, not limited to design, requirements, testing and development until the successful rollout of the integration with the application.

Security Advice

1. Design and implement *Security Access Matrix* (SAM) according to the roles. The SAM Mapping shall be developed together with HDC during the implementation; and
2. Support for Access and Controls, Security and User & Group Management with mechanisms to protect the information such as, but not limited to, role-based access control (i.e. tiered

permission), assigned privileges (i.e. add, edit, delete and view only), data loss prevention, prevents multiple logins within a stipulated period of time and data security.

Test Execution & Management

1. Vendor shall devise the test plan, test basis, test cases and other related documents according to the test levels and test types. These documents will be reviewed with HDC for agreement and signing off;
2. The test levels/ test types should cover but is not limited to the following :-
   - Development/Unit Test;
   - System Integration Test;
   - User Acceptance Test;
   - Final Acceptance Test (3 months period after go-live); and
   - Performance Test and all other project testing phases required as part of the project and its required documentation.
3. Vendor is required to perform a system load test to measure the load that can be handled by their proposed system; and
4. Vendor to provide application stress test to determine the application's robustness, availability and reliability under extreme conditions.

Documentation/Manual

1. Provide documentation (hardcopy/softcopy) for the following areas should comply with MS ISO 9001:2015 standard quality:
   i. Training materials;
   ii. Technical operations manual;
   iii. User manual;
   iv. Administration manual;
   v. Project Documentation;
   vi. System & Operational Manuals;
   vii. Test Documentations;
   viii. All other related manuals; and
   ix. Project Management Plan documentation which should include the following:
      - Background;
      - Scope;
      - Work Breakdown Structure (WBS) and its Dictionary;
      - Deliverables;

- Implementation plan;
- Project Organizational Chart;
- RACI Matrix of the Vendor;
- Foreseeable Project Risks;
- Communication Plan;
- Project Timeline; and
- Project best practices.

Communication, Change Management and Training

1. Provide all relevant services in commissioning the project, not limited to, the change management processes and deliverables;
2. Provide the necessary training for HDC end users, administrators and key persons that will be involved in this project. Conduct Train–the trainer sessions with identified stakeholders during the implementation. The number of the sessions shall consider the numbers of participants and locations of the participants; and
3. To develop online training material such as online tutorial for external users.

Project Management and Implementation

1. Provide *Project Management* in the implementation for the whole solution including implementation and communication strategy. Project Manager must be the single point of contact and the one to have an overall overview of the smooth implementation of the project. In case of multiple Vendors, the Project Manager will have to be accountable;
2. Project Management will be using PMBOK, Agile or other equivalent methodology that are deem to be the best fit for the project implementation strategy; and
3. Post Implementation Review within 3 months of the final acceptance. Project Closure and Post Implementation Review will be reviewed upon agreement with the selected vendor.

Support and Maintenance

Propose *post implementation* support coverage for:

1. On-going (software and support/maintenance services);
2. Software Warranty, if applicable; and
3. Provide and maintain all necessary hardware, software, and all licenses (if applicable) required for 3 years.

Release 1

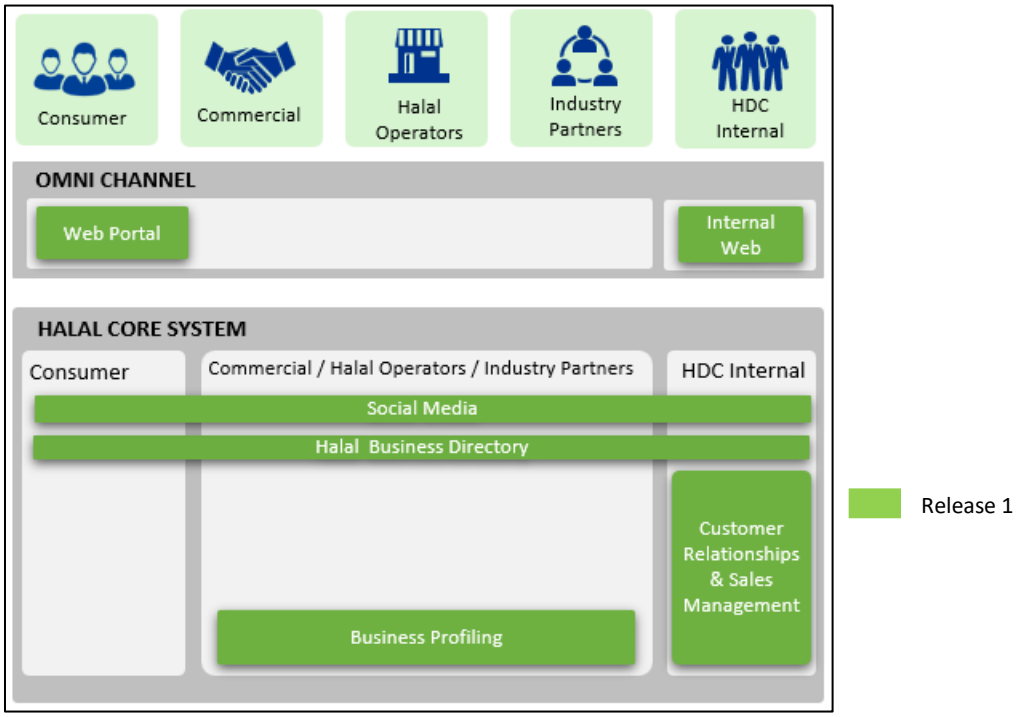


Figure 1: Release 1 Scope of Work

The above diagram depicted the **Release 1** modules for this project. The description of the modules is explained below:

1. **Web Portal** - The web portal is a series of web pages, images, information, updates, and other digital assets that can be accessed through the internet on a web server. It would be accessible, user-friendly, simple, and contains basic information just to entice the public to register with HIP and experience the benefits as HIP subscribers. It also embarks on HIP partner's advertising and marketing as well as attracts a service provider to register and collaborate with the HIP. The web portal will lead any visitor to register or sign in to the Internal Portal to acquire more Halal information, request a Halal service, participate in the Halal program, and more.

2. **Internal Web** - The Internal portal is a one-stop centre for all the e-Services and also as a virtual communication channel for the HIP to share useful information and current update to the public. There is different access for HDC members (Management, RGU, and HDC members) and HIP members

(paid or free users) hence, the dashboard (in the main page) view would be different for each type of access. However, to use all the features in Internal Portal HIP members need to subscribe hence, HIP could generate revenue from the membership. This single sign-on (SSO) platform would provide features business, and services from HDC members and HIP partners. It also embarks on advertising and marketing offers for all portal subscribers. The display on the main page would allow HIP members to view and manage their task, submitted application, the status of their helpdesk ticket, search content, and change language. This Internal portal is like a virtual mall. The HIP member's data captured in the portal would be utilized by Business Intelligence then, helping the members to provide information via many features such as dynamic dashboard, ads personalization, report, and more to make a decision as well as improves business.

3. **Social Media** - HIP Community uses a concept same as other social media such as Facebook to interact with people, share information, and engage in any events. However, the HIP community is only exclusive to HIP members and not open to the public like other social media. Its purpose is to attract potential clients, obtain feedback, increase market reach, getting the latest Halal industry news, develop customer networks, advertising, and branding. This social media platform should be able to highlight all vital discussions or events between HDC and HIP members as well as linking with each other.

4. **Business Profiling** - HIP members need to fill up the Business profile in order to utilize the data and display it in the Business Directory and business page. A Business Profile will capture basic information, organization information, service, and product list, as well as financial performance. HIP rating is given based on the information filled in the Business Profile. While, Business Page will display the basic and service or product list information. It is also a platform for HIP members to publish marketing collateral that may create a lead between the members through the HIP. This business profiling is one of the features that would enhance Business Intelligence.

5. **Halal Business Directory** - It is a platform comprises of two key features they are the search engine that allows user to search using keywords and directory that allow users to browse the information using the defined taxonomy. The taxonomy would consider a filter by state, industry, type of product, and certified Halal JAKIM. A search engine will be able to perform these multiple criteria. This section

would provide a HIP member with a list of companies with a basic description based on the taxonomy selection and keyword search. It would generate another section which is a Business Profile.

6. **Customer Relationship Management (CRM) and Sales Management** - It aims to maintain and enhance customer service relationships between HIP members and HDC business growth. HIP would manage all records of HIP stakeholders to manage sales activities, enrolment in any program, or any inquiries. It also allows the HIP to provide insight on areas of opportunity and demand of the Halal industry as well as enhance customer satisfaction. Technically, HIP and RGU would have a CRM dashboard to manage a lead and task.

Release 2

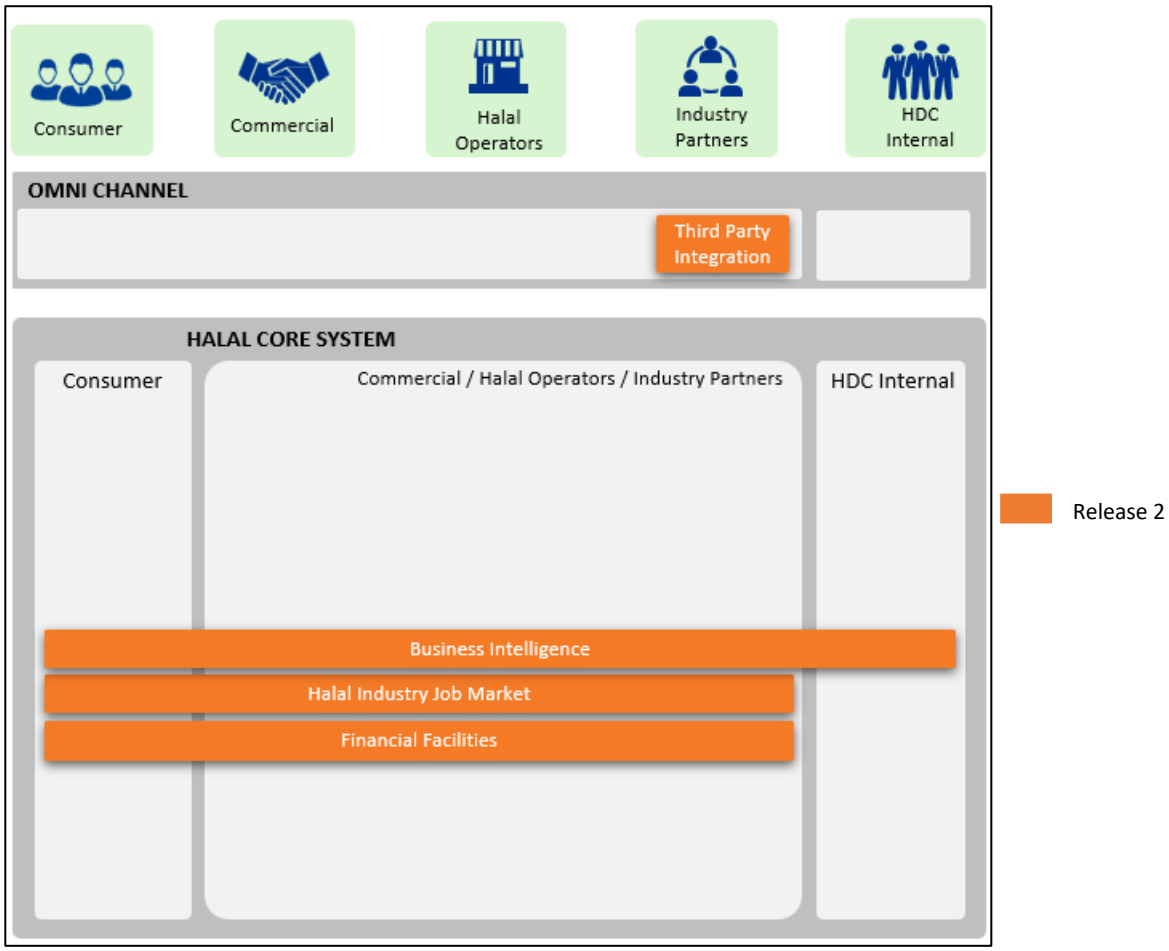


Figure 2: Release 2 Scope of Work

1. **Third Party Integration** - It is a connection between two or more apps that is built on an external platform. Other systems will integrate with HIP to send the information to HIP or retrieve the information from HIP to complete the process. Third party tools help to improve HIP member experience become more easily find products and more quickly. Besides that, it helps for monitoring and reporting purposes for RGU user and helps for better understand for decision making.

2. **HDC Programs** – It comprises the list of HDC existing applications which are Halal Incubation Project for Entrepreneurs Program (HIPER), Halal Knowledge Center (HKC), Digital Augmented Showcase of Halal Malaysia (DASH) and Halal Ingredient Database (HIDB). HIP platform will integrate with these systems in order to extend the offering and services to HIP members seamlessly. Below are the details on the system mentioned:

- **HKC** as the leading Halal knowledge purveyor and custodian for academic researches, industry insights, and economic studies that relays the Halal Economy impact.
- **DASH** is an integrated digital platform that delivers a combination of Augmented Reality capabilities through 3D enabled presentations of Malaysian Halal products and services.

3. **HIPER** - Main target is to catalyse the growth of Halal enterprises. Compared to other incubation programmes that look into providing physical office space and financing assistance, HIPER looks at providing business consultancies and advisories to its participants.

4. **HIDB** - Repository for Halal Ingredient products and services where member able to find the product and services required on it.

5. **Strategic Partners** – Strategic partners are HIP external stakeholders who were identified to compliment and support HIP services offerings. Through the services and offerings by the strategic partners, it will assist and facilitate the growth of HIP members. Currently below are the identified strategic partners in HIP:
    - **SMEXpert** by Bank Islam is created with the aim of improving business practices through financial inclusion. It is a mobile application dedicated to support the SME ecosystem to enable SMEs to grow their business with ease by having the right knowledge, customised financial support and international Halal market outreach.
    - **HIP Percipio** is an online learning platform that offers Halal Training content together with 8,500 learning content. It enables organizations to access curated content including proprietary resources and assets from other sources. It leverages highly engaging content, curated into learning paths including Halal related contents that are contents that are periodically updated to ensure continuous access to the latest information.
    - **PayHalal** is a syariah compliance payment gateway service that allows HIP member to perform online payment transaction for both HIP platform and HIP mobile app. With PayHalal, user can be assured of safety, speed and absolutely no riba.

6. **Financial Facilities** - It is a financial package offered by financial instituitions such as banks and peer-to-peer lending institutions to assist HIP members in terms of providing financial aid. There are varies financial offerings including Halal certification financing, Export financing and others. As of now the

financial instituition which offers financial facilities are Bank Islam, Microleap, jomSettle and many more will be joined in the future.

7. **Halal Industry Job Market** - Integration with talentxchange to serve the platform between job seeker and recruiter to find the job opportunity and resource required. This is similar concept with other job search platform like JobStreet and Monster. However, Halal Industry Job Market only applicable for HIP members.

8. **Business Intelligence** - This system will provide insight, trend and visibility of Halal Industry and Market based on data collected in HIP. The data can be used to produce publication or assist HDC in monitoring the growth or the trend of Halal industry in Malaysia.

Release 3

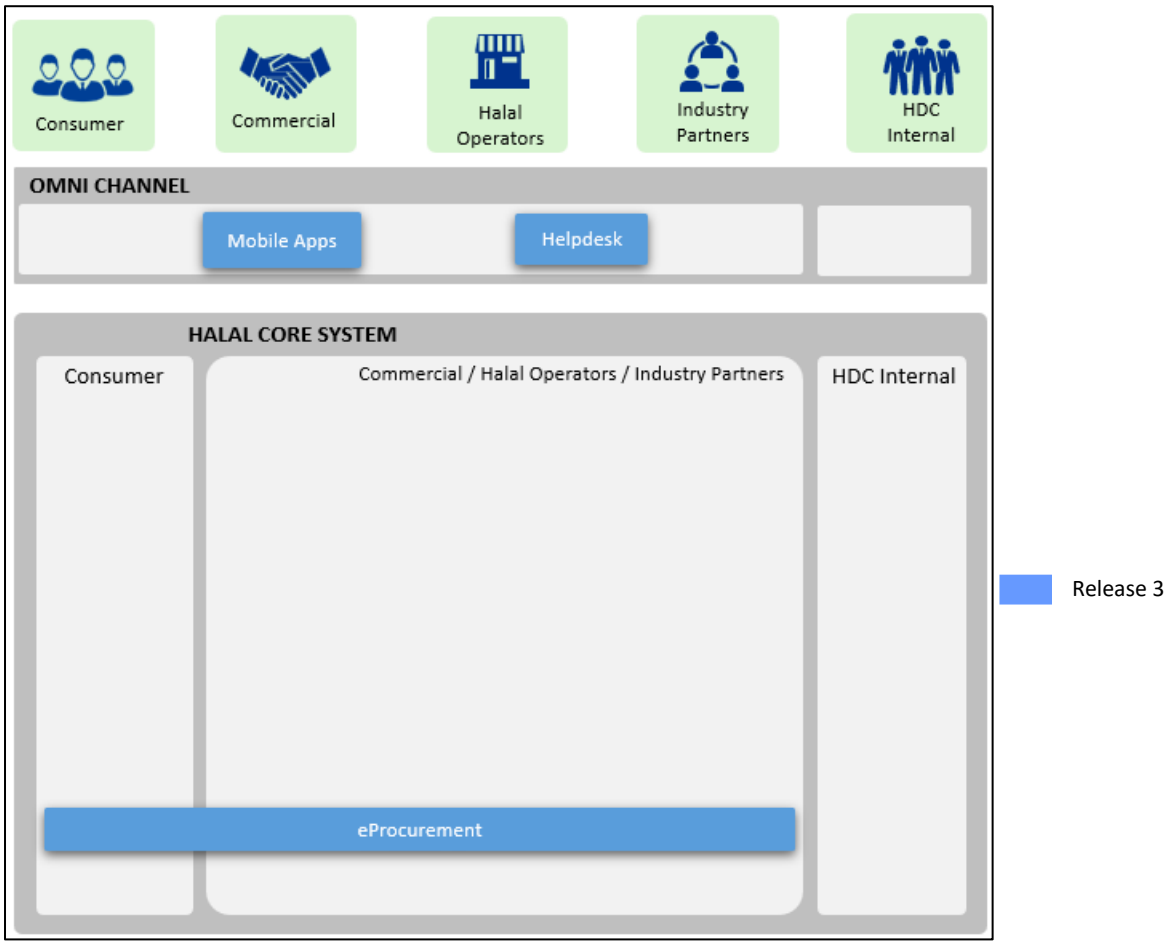


Figure 3: Release 3 Scope of Work

1. **Mobile Apps** – Mobile app is a type of application software designed to run on a mobile device, such as smartphone or tablet computer. The mobile version focuses more on providing accessibility of information through mobile devices. The feature will be limited to critical information such as Halal Business directory, social media, Market place, Halal knowledge center and others.

2. **eProcurement** – eProcurement also known as an electronic procurement or supplier exchange, is the purchase and sale of supplies, equipment, works and services through a web interface or other networked system. The technology is designed to centralize and automate interaction between an organisation, customers to improve the efficiency of procurement practices. HIP provide this platform

between organization and supplier who are register as HIP member to suit the requirement between both parties.

3. **Helpdesk** - There is a group of people who will provide assistance and information that is related to the HIP website, product/services or general enquiries that might be asked by users. This team will reach users either by email or through phone call and will assist users based on their needs.

Release 4

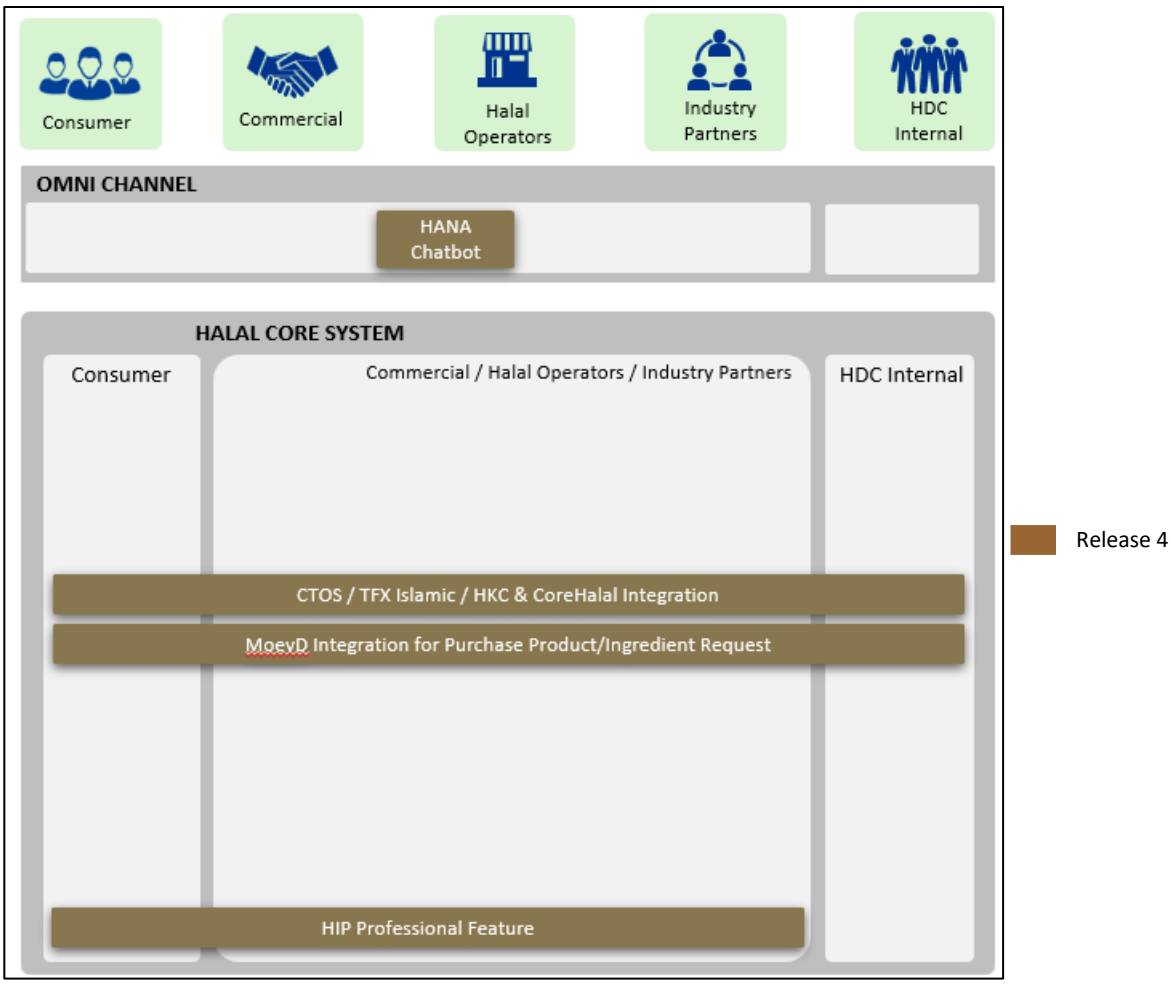


Figure 4: Release 4 Scope of Work

1. **HANA Chatbot** – HANA Chatbot is an application used to conduct an online conversation via text instead of providing direct contact with a live human agent. It is a type of software that can help customers by automating conversations and interact with them through messaging platforms. HANA Chatbot is used in dialog systems for customer service purpose.

2. **HIP Integration** – There have a few parties cooperate with HIP and require some integration setting to ensure the functions are working fine. Below are the parties involved with HIP integration:

    - **CTOS** provides the report for the HIP member to purchase either for their own company or for other HIP member/ non-HIP member reports. The integration between HIP and CTOS is required in a way to request the report from HIP to CTOS and the report submission from CTOS to HIP.
    - **TFX Islamic** provides the report for the HIP member to purchase either for their own company or for other HIP member/ non-HIP member reports. The integration between HIP and TFX is required in a way to request the report from HIP to TFX and the report submission from TFX to HIP.
    - **HKC** provides single sign on with HIP that allows HIP member to login with a single ID between these two platforms. In other words, single action provides same effect by passing the token seamlessly between HIP and HKC.The integration consists of login, logout, register new user, search user, reset password and activate account.
    - **CoreHalal** provides single sign on with HIP that allows user with HIP Pro role to login with a single ID between these two platforms. In other words, single action provides same effect by passing the token seamlessly between HIP and CoreHalal. The integration consists of login, logout, register new user, search user, reset password and activate account.
    - **MoevD** provides single sign on with HIP that allows HIP member to login with a single ID between these two platforms. In other words, single action provides same effect by passing the token seamlessly between HIP and MoevD. The integration consists of login, logout, register new user, search user, reset password and activate account to proceed with bulk purchase in MoevD.

3. **HIP Professional Feature** - Provides additional feature for user who subscribe the HIP Pro. The features covered including notification of product/services certificate expired, view extra informations of other company details, integration with CoreHalal, download data in HIP Analytics dashboard, download product/service's certificate and download product/services searching result in pdf format.

The features listed below have been mutually agreed upon by both parties to be enhanced in order to meet the functional requirements of the platform. The following table outlines the original modules, the corresponding replacement modules, and the rationale for each change.

No.	Original Module	Replacement Module	Reason of Change
1.	SME Assist Integration	Business Solution	SME Assist is a third-party application that is currently not ready for integration. To streamline operations and consolidate functionalities, we are transitioning to a unified module that supports all HDC services.
2.	microLEAP Integration	CTOS	As SME Assist is a third-party system and not currently available for integration, a new module has been developed to incorporate CTOS features, including the capability to generate CTOS buy reports.
3.	EasyStore Integration	HTI	Due to EasyStore is a third-party system and not currently available for integration, we have proposed to create a dedicated page within our internal HTI module to record and manage training attendance specifically for the training attendees.
4.	TFX Islamic Integration	Business Profile and Product Search Feature	TFX Islamic, being a third-party application, is not currently available for integration. Consequently, we developed an internal solution featuring a business profile and product search functionality to allow users to browse the relevant database efficiently.
5.	Purchase Request/ Product Request/ Ingredient	MoevD	The original plan was to create an interactive button that can connect the HIP Member to their selected company to purchase order. However, this was replaced by identifying an external B2B solution, MoevD that facilitates bulk ordering of vendor products interactively.

6.	Halal Professional Feature	HIP PRO	Since integration with the third-party provider for the Halal professional data could not be achieved, the functionality has been replicated and enhanced within the HIP PRO module.
7.	HIPER	HART	We have renamed HIPER module to HART – Halal Accelerator Tool for clearer functionality.

Table 2: Replacement Modules Release 4

Release 5

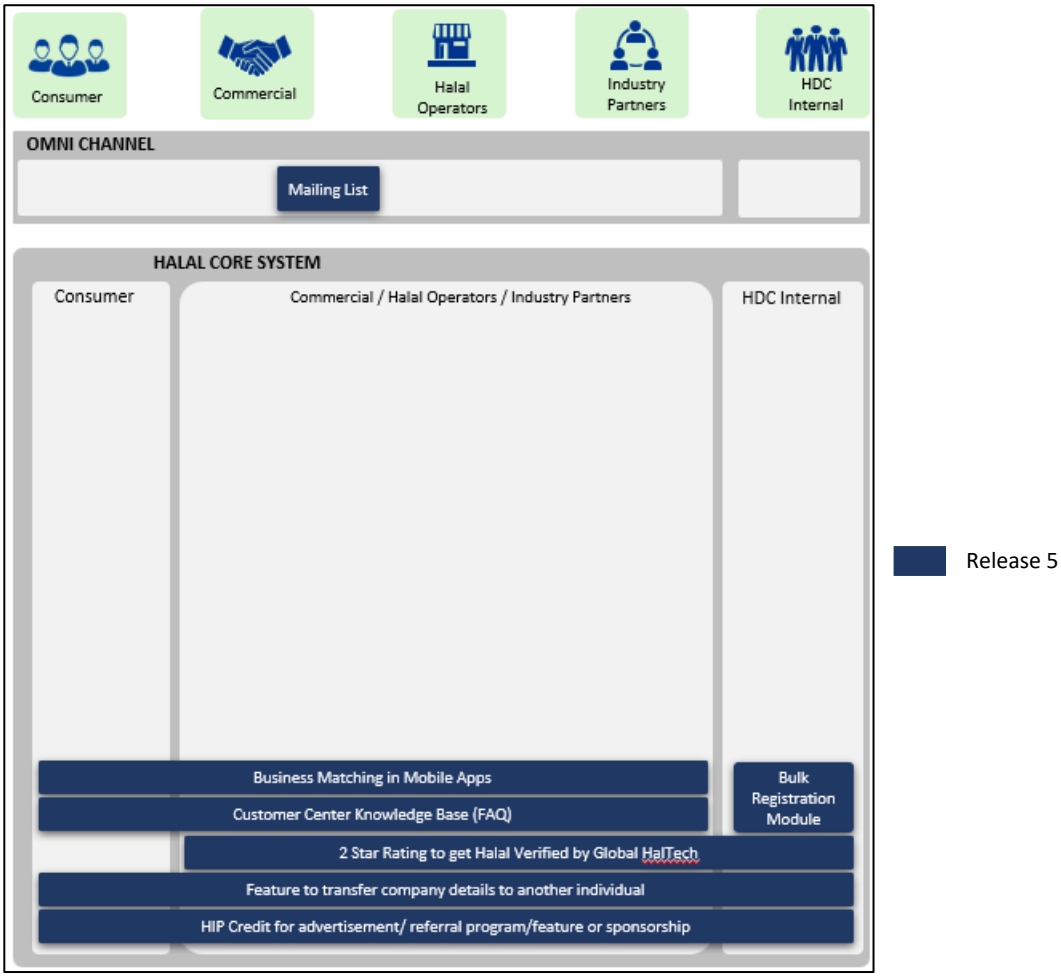


Figure 5: Release 5 Scope of Work

1. **Mailing List** – This is a feature to blast an email among HIP member by HIP Admin. This purpose is to send some information to the member. HIP Admin able to filter the recipient before send the email and download the list into excel format.

2. **Business Matching in Mobile Apps** – This feature applicable in Mobile Apps to find the business required and system will do some screening to display the business matching that suite with the requirement. HIP member able to slide right to accept or slide left to reject the business matching.

3. **Customer Center Knowledge Base** – This feature act as a repository of information related with HIP's module. HIP member able to search and refer to this menu to look into FAQ and give comments and rate on the article posted. This menu will be managed by RGU user and HIP Admin to post the useful article to ease HIP member experience while using HIP system.

4. **Bulk Registration Module** – Provides user registration in bulk through excel file before upload to the system by HIP Admin. This feature is very helpful to HIP Admin and save time.

5. **2 Star Rating verified by Global HalTech** – Company rating when acknowledges Halal verified by Global HalTech. This rating is helpful to represent the good company profile and is viewable among other HIP member.

6. **Feature to transfer company details** – This is a feature to transfer business profile information to the new person in charge and will removed the company details from previous person in charge account. This is very helpful feature to avoid user from re-enter the company profile information.

7. **HIP Marketing** – This is the services provide by HIP including advertisement video, poster, banner, referral program, sponsorship and etc. The services come into a few packages that allow member to choose accordingly.

The features listed below have been mutually agreed upon by both parties to be enhanced in order to meet the functional requirements of the platform. The following table outlines the original modules, the corresponding replacement modules, and the rationale for each change.

No.	Original Module	Replacement Module	Reason of Change
1.	Business matching for Mobile Apps	Semantic Search & Meta Search	The current module has limited matching capabilities. The new Semantic Search & Meta Search will give users faster and more accurate results
2.	Customer Center Knowledge Base	Knowledge Help Center	The current knowledge base has limited search and support features. The new module offers easier access to information and guided help for users.
3.	eMarketplace	HIP Marketing	The eMarketplace lacks marketing tools and integration with our platform. The new HIP Marketing page allows us to manage promotions and training announcements effectively.
4.	HIP Credit for Ads	Online Learning	We are replacing the ad credit module with online learning to equip SMEs with marketing and digital skills, enabling them to run effective promotions themselves in the future.
5.	2 Star Rating	Recommended List	Replacing the star rating with a recommended list will guide users toward high-quality vendors, preparing them for seamless future bulk purchases.

Table 3: Replacement Modules Release 5

Deliverables

In the table below described the main project milestones and the completion dates for each milestone.

The details of the milestones will be described later on this section.

Table 4: List of Modules

No.	Release	Modules	Completion Date
1.	Deployment Release 1	• Portal • Internal Portal • Business Profile • Social Media • CRM	29th May 2022
2.	Deployment Release 2	• SMEXpert • Integration eMarket Place • HIPER • Halal Knowledge Centre • DASH • Halal Ingredient Database • HIP Percipio • PayHalal • Business Intelligence	10th June 2022
3.	Deployment Release 3	• Mobile Apps • eProcurement • HIP Rating	29th July 2022
4.	Deployment Release 4	• HANA Chatbot • Integration SME Assist • Integration Micro Leap • Integration Easy Store • Integration TFX Islamic • Purchase Request/Product Request/Ingredient • Halal Professional Feature	10th September 2022
5.	Deployment Release 5	• eMarketPlace • Customer Knowledge Help Centre • Business Matching • Feature to transfer company details to another individual • 2 Star Rating to get halal Verified by Global Haltech	23rd September 2022

No.	Release	Modules	Completion Date
		• HIP Credit for advertisement / referral program/feature or sponsorship • Bulk Registration Module • Mailing List	

Certificates

Below are FAT certificates for each module delivered in Production environment.

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform - Portal (Release 1) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Internal Portal (Release 1) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Business Profile (Release 1) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Social Media (Release 1) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Customer Relationship Management (Release 1) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – SMEXpert App Integration (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – eMarketPlace Integration (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – HIPER (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Halal Knowledge Center (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Digital Augmented Reality Showcase of Halal Malaysia (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platf...		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Halal Ingredient Database (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – HIP Percipio (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – PayHalal (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Business Intelligence (Release 2) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Mobile Apps (Release 3) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – eProcurement (Release 3) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – HIP Rating (Release 3) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – HANA Chatbot (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – SME Assist Integration (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – MicroLeap Integration (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – EasyStore Integration (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – TFX Islamic Integration (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Purchase Request/Product Request/Ingredient (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Halal Professional Feature (Release 4) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – e-MarketPlace (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Customer Center Knowledge Base (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Business Matching for Mobile Apps (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Feature to Transfer Company Details (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – 2 Star Rating to get Halal Verified by Global Haltech (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamali Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – HIP Credit for Advertisement/Referral Program/Feature or Sponsorship (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)

Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Bulk Registration (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022

Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamalud... Head Of Halal Integrated Pla...		7/10/2022

FINAL ACCEPTANCE TEST SIGN OFF (FAT)


Signed off on behalf of the Hyper Analytics Sdn Bhd

The document acknowledges that Halal Integrated Platform – Mailing List (Release 5) test activity has been completed and signed off by Halal Development Corporation (HDC).

Name and Title	Signature	Date
FADZUAN BIN ARBAIN Chief Executive Officer		6/10/2022


Signed off on behalf of the user from Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Ema Juliany Jamaluddin Manager Halal Integrated Platform		7/10/2022

Signed off on behalf of the Halal Development Corporation (HDC)

Herewith I/We certify that all the test and acceptance activity attached is done and completed successfully.

Name and Title	Signature	Date
Mohammad Hafiz Jamaluddin Head Of Halal Integrated Platform		7/10/2022
